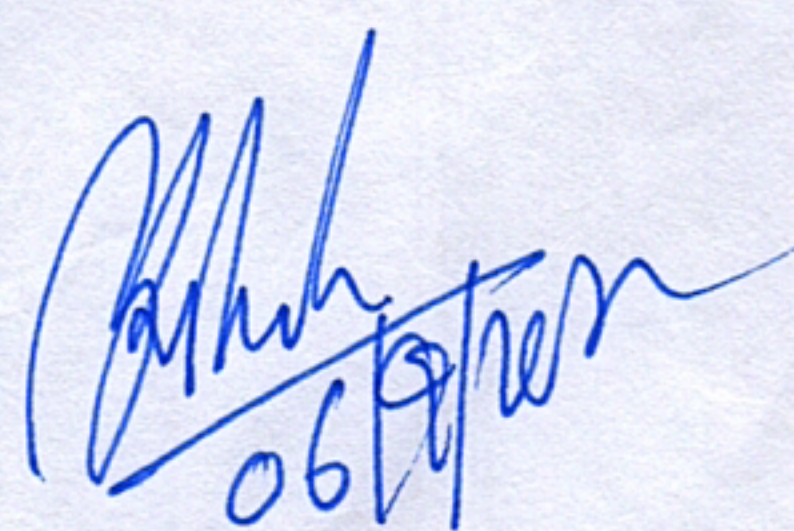


DETAILS OF PROJECT

Sl. No	Name of Contract	Project Cost	Name of Contractor	Amount of Contract	Date of Completion
1	Construction of Faculty building of Social Science and Languages (First Floor) at Rajiv Gandhi University, Rono Hills, Doimukh	17.89 Crore	M/S Good Will Suppliers, Itanagar	12.30 Crore	30 th July, 2022 (Building)
	Ramp, Staircase(External) Car Parking area, Furniture, equipment & other contingency expenditure (To be executed after release of fund)			5.59 Crore	
2	Construction of Faculty building of Department of Education (First Floor) at Rajiv Gandhi University, Rono Hills, Doimukh	8.50 Crore	M/S Yowa Jyoti, Doimukh	6.03 Crore	05 th March, 2022 (Building)
	Ramp, Staircase(External) Car Parking area, Furniture, equipment & other contingency expenditure (To be executed after release of fund)			2.47 Crore	
3	Construction of Faculty building of Mass Communication and Computer Centre (First Floor) at Rajiv Gandhi University, Rono Hills, Doimukh	4.95 Crore	M/S Yowa Jyoti, Doimukh	4.15 Crore	23 rd February, 2022 (Building)
	Furniture, equipment & other contingency expenditure (To be executed after release of fund)			0.80 Crore	
4	Construction of Faculty building of Zoology Department (Ground Floor) at Rajiv Gandhi University, Rono Hills, Doimukh	7.63 Crore	M/S Tana Tahin, Doimukh	6.39 Crore	Work in Progress (Building)
	Car Parking area, Furniture, equipment & other contingency expenditure (To be executed after release of fund)			1.24Crore	


 Executive Engineer
 कार्यपालक अभियंता
 Executive Engineer
 राजीव गांधी विश्वविद्यालय
 Rajiv Gandhi University
 रोनो हिल्स, दोइमुख
 Rono Hills, Doimukh

**RAJIV GANDHI UNIVERSITY
RONO HILLS, DOIMUKH-791112
ARUNACHAL PRADESH**

1. Last Three Years Details

(a) Completed Projects as on 1st September, 2022.

Sl No.	Project Name	Contract Bid Date	Date of Award of Contract and Contractor	Contract Amount	Total amount	Date of Completion	Sources of Funding	Remarks
1	Faculty Building of Social Sciences & Languages(First Floor) at RGU	17/06/2019-02/07/2019	10/10/2019 M/s Goodwill Suppliers, Itanagar	Rs. 12.30 crore	Rs. 12.30 crore	30 th July, 2022	UGC	
2	Faculty Building of Mass Communication and Computer Science(First Floor) at RGU	17/06/2019-02/07/2019	10/10/2019 M/s Yowa Jyoti, Doimukh	4.15 crore	4.15 crore	23 rd Feb., 2022	UGC	
3	Faculty Building of Education (First Floor)at RGU	17/06/2019-02/07/2019	10/10/2019 M/s Yowa Jyoti, Doimukh	6.03 crore	6.03 crore	5 th March, 2022	UGC	

ka

(b) Ongoing Projects (HEFA/UGC) as on 1st September, 2022.

Sl No.	Project Name	Contract Bid Date	Date of Award of Contract and Contractor	Contract Amount	Project Completed in %	Date of Expected Completion	Sources of Funding	Remarks
1	Faculty Building of Zoology Department at RGU(Ground Floor)	05/02/2021-12/02/2021	23/03/2021 M/s Tana Tahin	7.63 crore	95%	04/10/2022	UGC	Work in progress

Link :- <https://eprocurement.gov.in> .

[Signature]
22/9/2022

**Executive Engineer
Rajiv Gandhi University (CU)**


(c) Ongoing Projects (HEFA) as on 1st September, 2022.

Sl No.	Project Name	Contract Bid Date	Date of Award of Contract and Contractor	Contract Amount	Project Completed in %	Date of Expected Completion	Sources of Funding	Executed by
1	Faculty Building for Electronic and Communication	04.02.2022	09.03.2022, M/s Tana Hali Construction & Co.	2093.30	8%	31.12.2023	HEFA	CPWD
2	Extension of Main Library							
3	Utility Service Centre							
4	200 Seater Girls Hostel	17.02.2022	03.03.2022, M/s T.T. Enterprises	1503.51	28%	31.12.2023	HEFA	CPWD
5	200 Seater Boys Hostel	17.02.2022	02.03.2022, M/s Jumsi Enterprises	1503.51	28%	31.12.2023	HEFA	CPWD
6	Residential Quarter T- III 4 Blocks	27.01.2022	23.02.2022, M/s Dony Lella Enterprises	490.25	22%	31.12.2023	HEFA	CPWD
7	Residential Quarter T- IV (5 Blocks, 20 Unites)	17.11.2021	22.12.2021, M/s Hi Rise Infratech Pvt. Ltd.	849.29	30%	31.12.2023	HEFA	CPWD

(D) Ongoing Projects (EWS) as on 1st September, 2022.

Sl No.	Project Name	Contract Bid Date	Date of Award of Contract and Contractor	Contract Amount	Project Completed in %	Date of Expected Completion	Sources of Funding	Executed by
1	Girls Hostel 100 Seater	08.10.2021	04.12.2021, M/s Das Electric	772.00	55%	31.12.2023	UGC/MoE, Gol.	CPWD
2	Boy's Hostel 100 Seater	08.10.2021	04.12.2021, M/s Das Electric	772.00	32%	31.12.2023	UGC/MoE, Gol.	CPWD
3	Multipurpose Academic Building	05.05.2022	27.05.2022, M/s Toko Radh	1456.00	2%	31.12.2023	UGC/MoE, Gol.	CPWD

Link: - <https://www.tenderwizard.in> / CPWD


Executive Engineer
Rajiv Gandhi University (CU)
